



EUROPEAN CENTRAL BANK

EUROSYSTEM





EUROPEAN CENTRAL BANK

EUROSYSTEM



# **TARGET2-Securities**

## **Entering the Next Phase...**

**Marc BAYLE**

**Head of the T2S Project Team**

**European Central Bank**

**Meeting with representatives of market  
participants and market infrastructures**

**ECB, Frankfurt, 12 March 2007**

**Nothing in this presentation is  
carved in stone**

**It is the result of a first internal  
brainstorming of ideas**

**Input is welcome**


## T2S – entering next phase

1. Main objectives
2. Project Governance
3. Project organisation
4. Timetable

# 1- Main objective of the next phase: Define the T2S User Requirements

## Objectives of the next phase

- Consult the market on principles, needs and expectations
- Define the T2S User Requirements
  - In cooperation with all T2S stakeholders
- Prepare decision of CSDs to commit to T2S or not
- Prepare alternative access when a CSD does not want to join T2S, while some of its participants do
- Keep all stakeholders involved in the process
- Refine the cost/benefit evaluation



## Deliverables of the next phase


- T2S Principles
- T2S Functional User Requirements
  - Series of Consultation Papers
  - Final User Requirements
- T2S Non-Functional and Legal Requirements
- Revised T2S business case
- General functional specifications?

## T2S – entering next phase

1. Main objectives
- 2. Project Governance**
3. Project organisation
4. Timetable

## 2- Project Governance

Proposed governance for this phase

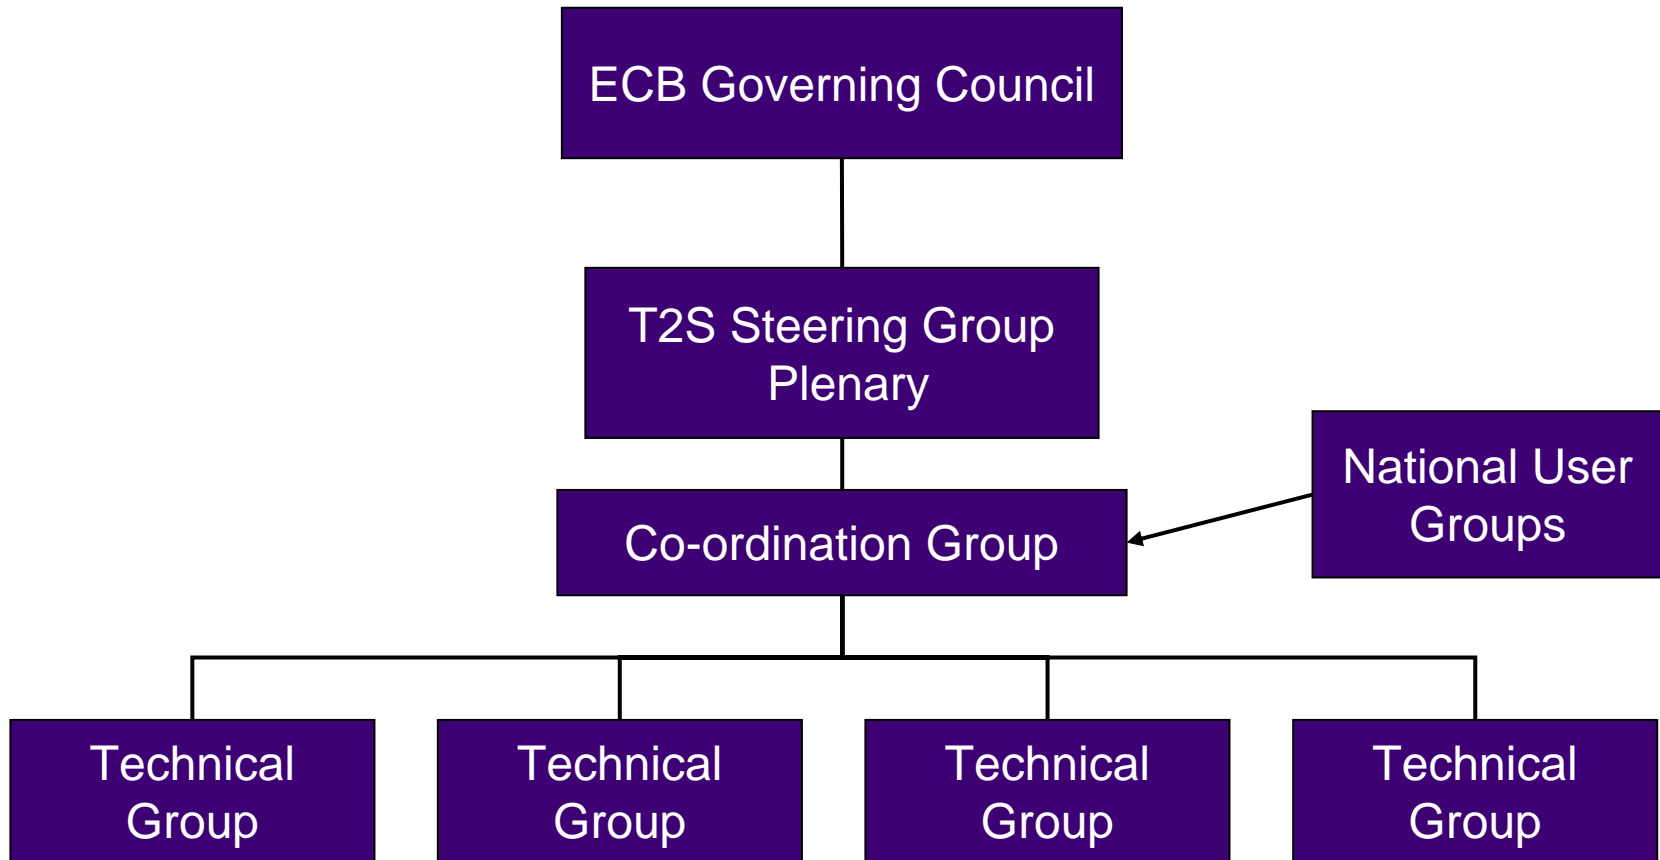

## 2- Project Governance

### Steering Group competencies

- Right of initiative in raising proposals to the Governing Council
- No filtering of proposals

(This does not affect the responsibility of internal bodies of the Eurosystem -e.g. PSSC- to advise the Governing Council. However they may not amend the proposals made by the Steering Group)



## 2- Project Governance

Possible composition of the Steering Group

**1/3 Central banks ?**

**1/3 CSDs ?**

**1/3 Users (mainly banks) ?**

- Decision in the substance
- Meets every 3 months

## 2- Project Governance

### The Steering Group

The issues:

- Which size ?
- Involvement of the non-euro area countries ?
- One size fits all (small versus big countries) ?
- Designation process: a nomination committee ?
- Which majority for decision ?

## 2- Project Governance

### Co-ordination Group

- Decisions concerning organisation of the work
- Meets once a month, just before TGs ?

Do we need a co-ordination group ?  
What composition ?

## 2- Project Governance

### Technical Groups

- To be defined according to the various workstreams in defining the user requirements (see next slides)

### National Groups

- To be set up by each NCB

## 2- Project Governance Remarks

- Framework to be discussed by PSSC end of March, **not yet approved** by the Governing Council.
- Details to be worked out: Everybody agrees that the Steering Group should be small, but everybody insists to be part of it.
- **May be different** for the subsequent phases of the project


## T2S – entering next phase

1. Main objectives
2. Project Governance
- 3. Project organisation**
4. Timetable



### 3- Project Organisation

Main focus is on the User Requirements, but legal and economic topics are covered as well

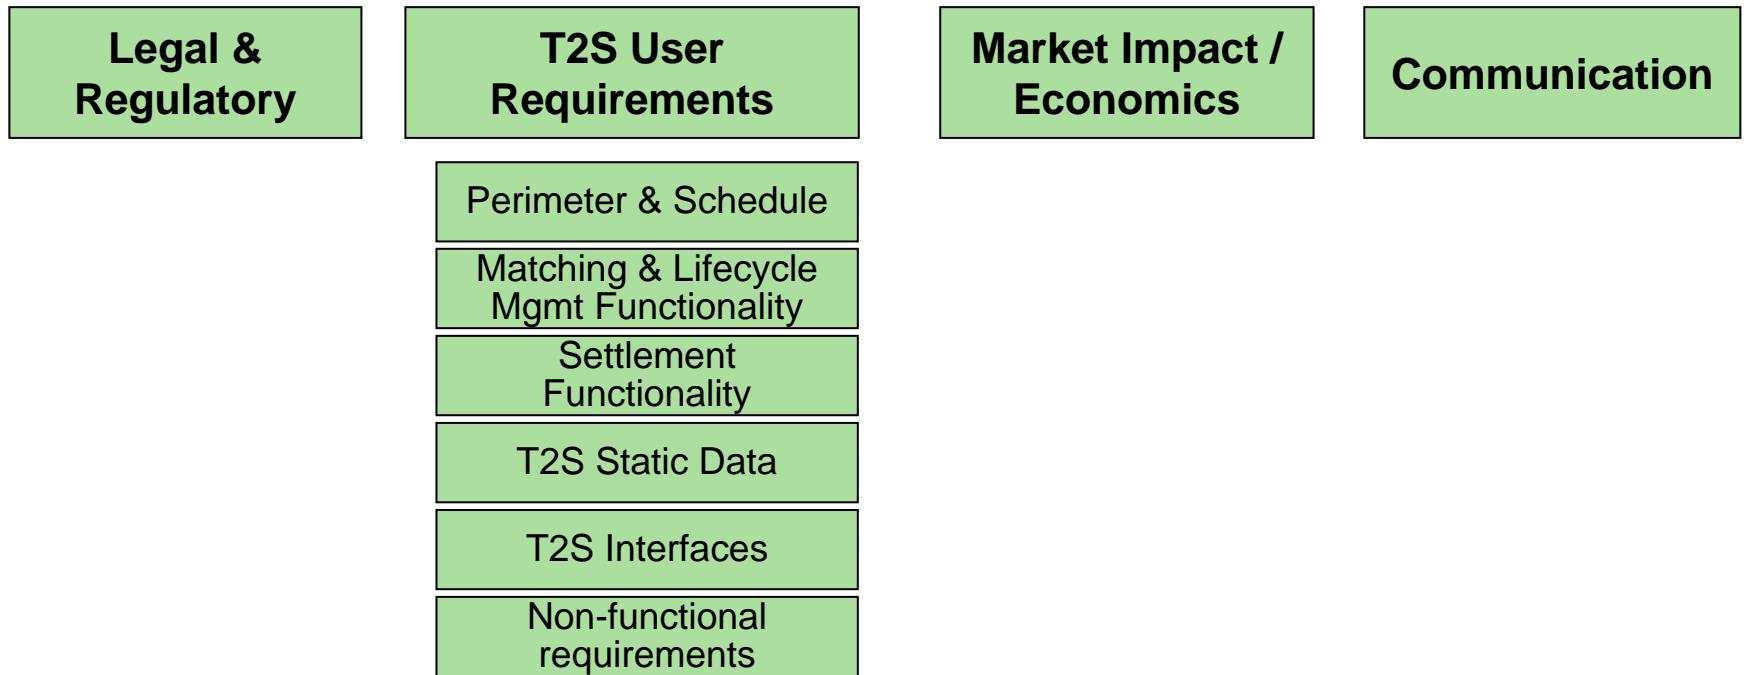



### 3- Project Organisation

Staffing support for the TGs in the ECB

- + **1/3 ECB**
- + **1/3 NCBs**
- + **1/3 Market**

ECB contracts (9 to 12 months)

- Consultants (market)
- ESCB staffs (central banks)





### 3- Project Organisation

Communication Stream to organise all aspects of T2S project communication

#### Scope

- Organise market consultation phase
  - Collect market feedback
- Keep stakeholders informed
  - EP, ECOFIN, regulators, etc.
- Public relations

#### Communication means

- Market consultation documents
- T2S Website
- T2S Newsletter
- Tri-party meetings
- Presentations to various stakeholders
- Technical Group meetings



## 3- Project Organisation

# User Requirements Stream dedicated to preparing the T2S User Requirements

### Perimeter & Schedule

- Cross Border Settlement
- Foreign currency settlement in T2S
- T2S Day / Operating Hours
- Start/End of day procedures
- Deadlines and timings

### Matching & Lifecycle Mgmt Functionality

- Validation & **Matching**
- Instruction management
- Instruction lifecycles
- Eligibility of instructions / deadline management
- Handling of cash instructions

### Settlement Functionality

- Settlement Model Batch and Real Time Structure
- Prioritization
- **Optimisation**
- Recycling
- Booking
- Self-collateralisation
- Collateral Management / relation with CCBM2

### T2S Static Data

- **Account Structure**
- Securities Reference Data
- Account Reference Data
- Customer Reference Data
- Market-specific Rules

### T2S Interfaces

- **Requirements for T2S-CSD Interaction**
- Requirements for interaction with TARGET2
- Direct / Indirect Access
- T2S User Interfaces
  - Securities instructions interface
  - Securities balance interface
  - Static data interfaces
- T2S Reports

### Non-functional requirements

- Security requirements (incl. availability and business continuity requirements)
- Capacity and performance
- Architecture requirements
- Operational requirements
- Standards

## 3- Project Organisation

### Legal/Regulatory and Economic Stream

#### Scope of Legal and Regulatory Stream

- **Work out contractual relationships between T2S owner, T2S operator and the CSDs**
- **Define legal requirements related to regulation of settlement**
- **General project support on legal matters**

#### Scope of Economic Stream


- **Refine project costs based on User Requirements**
- **Further refine the market impact analysis and the Business Case**

## T2S – entering next phase

1. Main objectives
2. Project Governance
3. Project organisation
4. **Timetable**



# 4- Indicative Consultation Timeline:

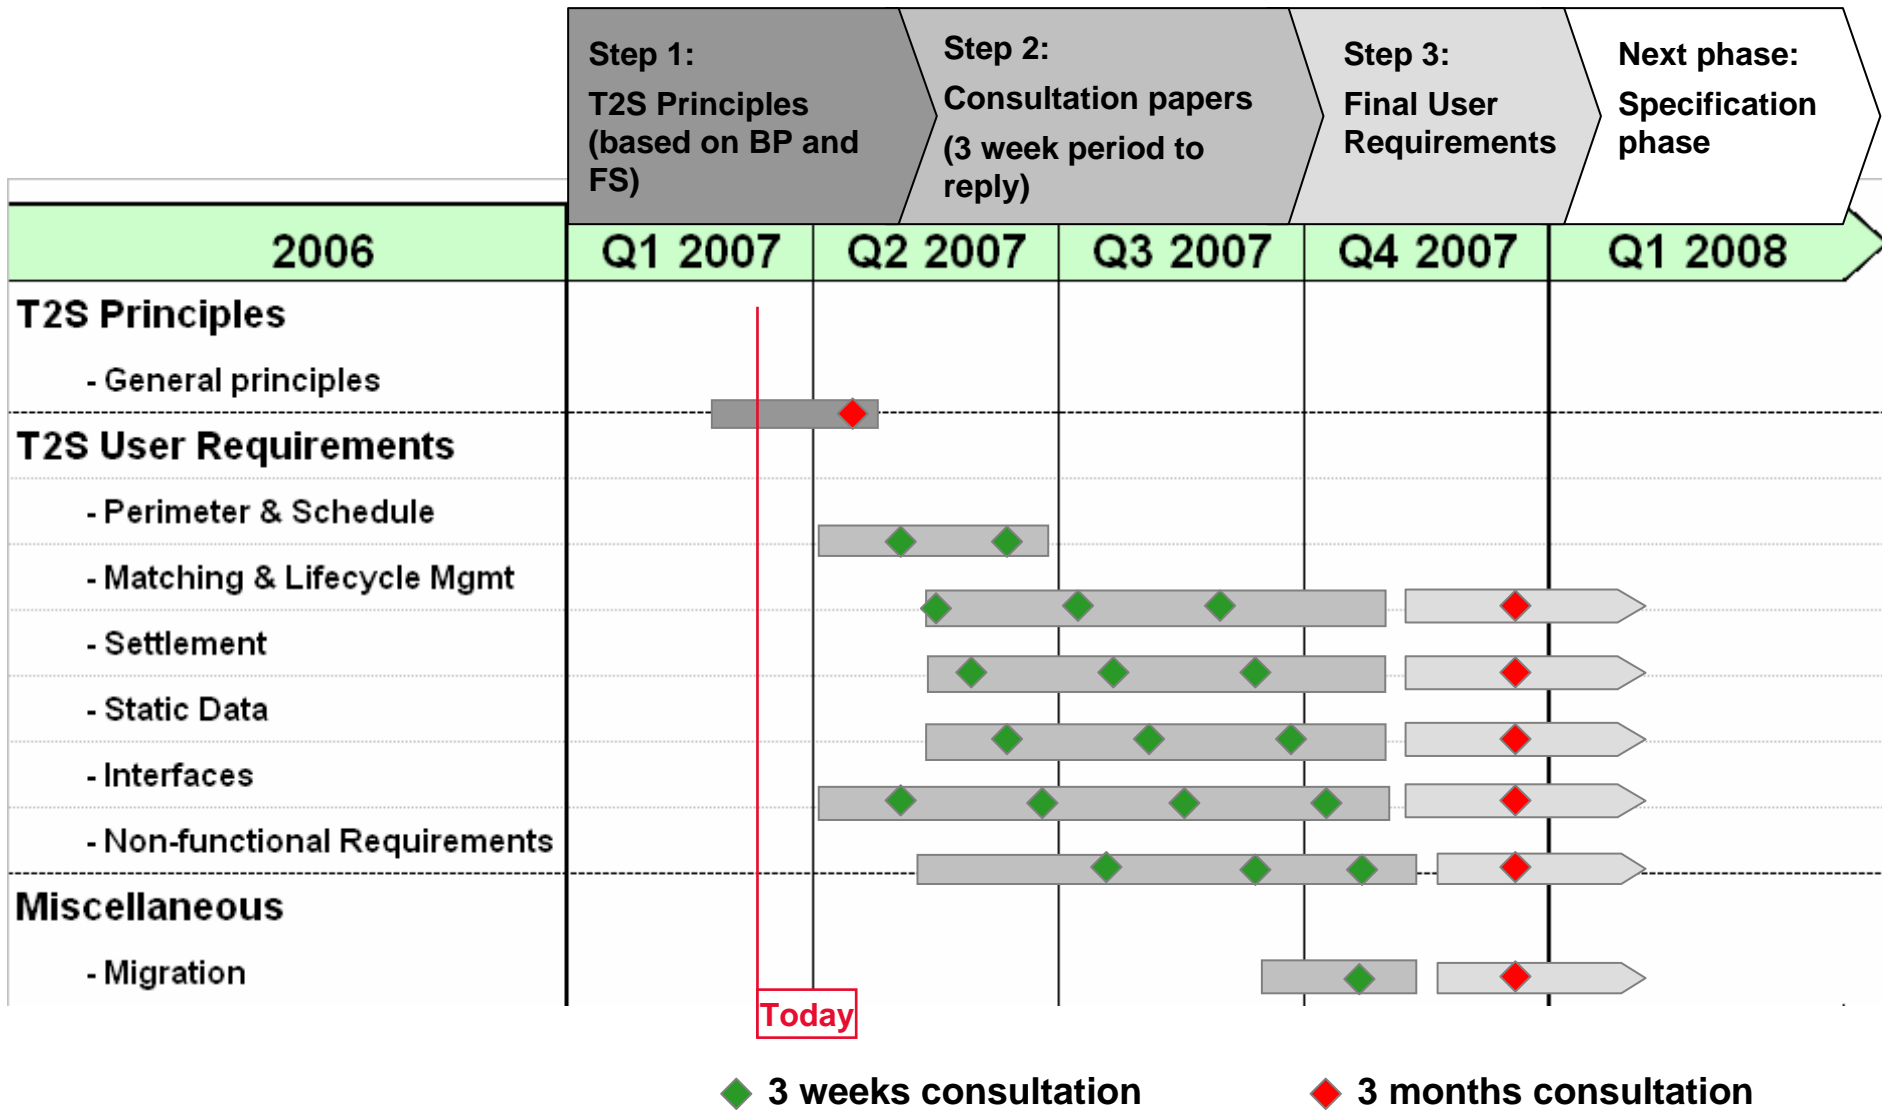



## 4- T2S Project timetable

### Next Steps

#### For the T2S Project

1. Ramp up project team
2. Define governance (Apr 2007)
  - Work out consultation and decision processes, to ensure involvement of stakeholders
3. Publish T2S Principles (Apr 2007)
4. Publish consultation papers on User Requirements (Start: May 2007)
  - Consultation papers
  - User Requirements

#### For the T2S Stakeholders

1. Express your priorities (Mar 2007)
  - What are the most important areas of the User Requirements?
  - What are the main criteria for the CSD commitment?
  - Where should the T2S project team put its focus first?
2. Prepare to be involved
  - Tight review schedule: 3 weeks!
3. Review, comment, and provide your expert input (Start: April 2007)



EUROPEAN CENTRAL BANK

EUROSYSTEM

